

IIS Platform Transition

AIRA Discovery Session March 28, 2016



CENTER FOR PUBLIC HEALTH PRACTICE
Oregon Immunization Program

2006 Environmental Scan

Blend Oregon's two immunization record systems

ALERT: Oregon's Statewide IIS

IRIS: Oregon's Local Health Dept. Medical Record System

Key Recommendations:

Integrate ALERT and IRIS

Explore COTS or GOTS solution

Explore external hosting and support

Potential barriers cited:

Sustainability/funding/staffing

System adoption barriers


Success Factor - Preparation

Saved \$\$ Contracted for environmental scan Contracted for Project Manager Involved Stakeholders Learned from those who went first





Success Factor - Perseverance



Manage expectations




Delays will happen





Success Factor - Patience

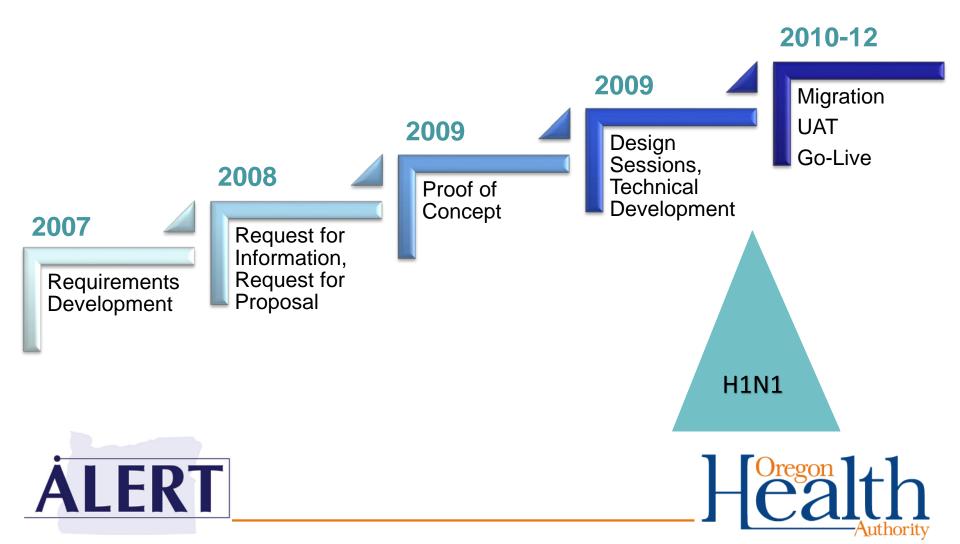

Lessons Learned – Stakeholder Involvement Critical at all stages

Staff Internal External National Support





Lesson Learned – Celebrate Milestones



RFP Complete



Legislation Passed



Contract Signed



Data Conversion and Migration Successful



UAT Started



UAT Complete



Training Videos Complete



Train the Trainer Successful



Roll Out Started



Phase 1 Complete



Phase 2 Complete




Roll Out - DONE





Lesson Learned – Evaluate

S

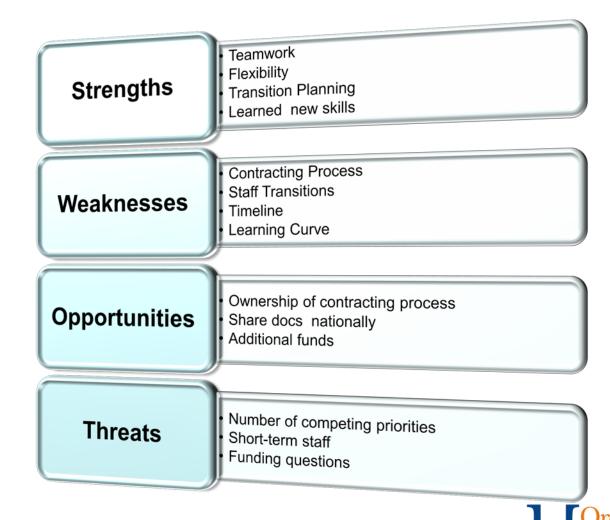



Resist recreating legacy system functionality

Communication is critical

Assumptions can derail progress

Process is necessary

My Question in 2009:



Will we ever get to the maintenance period?





My Question in 2016:



Does a maintenance period really exist?





